

WEEKLY PROJECT REPORT Report # 449A Week Ending: 10/14/2023

Project:
West Sider Park, Evansville, WI
 700 Porter Rd
 Evansville, Wisconsin, 53536



Project Team:

Owner:
 City of Evansville

Architect/Engineer:
 MSA

Aquatics Design:
 Water Technologies Inc

Athletic Field Specialists:
 Rettler Corporation

General Contractor:
 Corporate Contractors Inc (CCI)

Construction Start Date:
 08/30/2022

Construction Start:
 08/30/2022

Substantial Completion:
 04/30/2024

Work Completed Current Week

- 1) Roof trusses have been set on CMU walls of Bath House and cross bracing and brackets have been installed. Waiting for framing inspection.
- 2) Lazy River and lap pool has been backfilled around edges and framed for concrete island to be poured.
- 3) Installation of Sona Tubes for Sunshades are at 50% completed.
- 4) Masonry installation of 4 walls (3 exterior 1 interior) on the Equipment/ Pump House completed.
- 5) 65% of rubbing and patching of the interior Masonry is complete in the Bath House.
- 6) Installation of top tile of the Lazy River Pool is 80% Complete.
- 7) Install on Waterslide 60% of tubes and platform.
- 8) Sheeting of Roof of Bath House is 100% completed.
- 9) Plumbing rough in is 30% completed in the Bath House.
- 10) Framing out Concession stand walls is completed.

Work Scheduled Next Week:

- 1) Ongoing installation of exterior masonry walls on Pump House to completion.
- 2) Shingle Bath House Roof.
- 3) Install water Side run out pad.
- 4) Pour concrete for Sunshade structures
- 5) Prep for Trellis installation.
- 6) Installation of Bath House doorframes and doors.
- 7) Demo out existing old Bath House.
- 8) Set trusses on Pump house.
- 9) Put binder down Northside parking to Westside Bath House.
- 10) Install and finish Electrical room in Bath House to install Electrical panels on wall.



References

Photos (10)



Splash Pad

Taken on Oct 13, 2023, 8:53 AM CDT

Added on Oct 13, 2023, 9:27 AM CDT

Added by andrew gordon



Splash Pad

Taken on Oct 13, 2023, 8:53 AM CDT

Added on Oct 13, 2023, 9:27 AM CDT

Added by andrew gordon



Splash Pad

Taken on Oct 13, 2023, 8:53 AM CDT

Added on Oct 13, 2023, 9:28 AM CDT

Added by andrew gordon



Splash Pad

Taken on Oct 13, 2023, 8:53 AM CDT

Added on Oct 13, 2023, 9:27 AM CDT

Added by andrew gordon




Splash Pad

Taken on Oct 13, 2023, 8:52 AM CDT

Added on Oct 13, 2023, 9:28 AM CDT

Added by andrew gordon

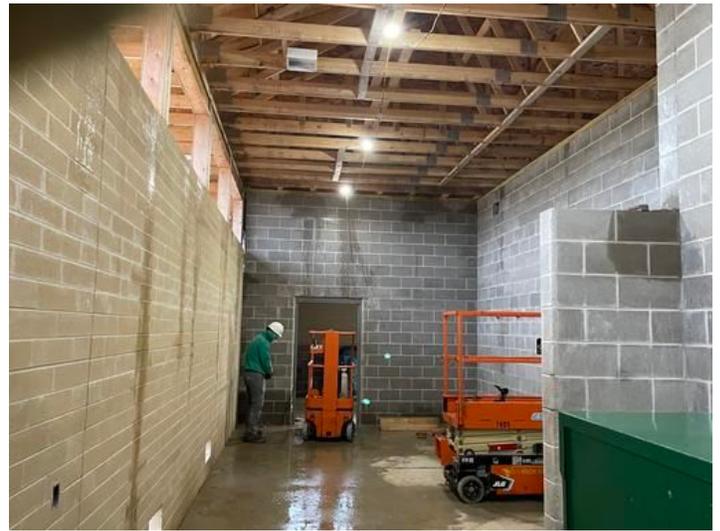

Interior Bath House clean up

Taken on Oct 13, 2023, 8:10 AM CDT

Added on Oct 13, 2023, 9:25 AM CDT

Added by andrew gordon



Interior Door setting in Bath House

Taken on Oct 13, 2023, 8:09 AM CDT

Added on Oct 13, 2023, 9:24 AM CDT

Added by andrew gordon



Interior Door setting Bath House.

Taken on Oct 13, 2023, 8:09 AM CDT

Added on Oct 13, 2023, 9:24 AM CDT

Added by andrew gordon



Sona tube installation for Sunshades.

Taken on Oct 11, 2023, 11:44 AM CDT

Added on Oct 11, 2023, 3:13 PM CDT

Added by andrew gordon



Installation of CMU on the Pump House.

Taken on Oct 11, 2023, 8:21 AM CDT

Added on Oct 11, 2023, 3:08 PM CDT

Added by andrew gordon
